Date 5-13-87 Permit No. 87-30

TOWN OF ACTON

APPLICATION FOR PERMIT TO CONSTRUCT WITHIN A PUBLIC WAY

This application must be submitted not less than five (5) days prior to any Construction within a public way.

Notice 24 hours in advance of any construction must be given to the Town Engineer.

1. Permittee: David C. Moulton Inc. Address: Skyfield Dr. Groton
2. Location of Proposed Construction: Intersection of Robert Rd + Puritan Rd.
3. Purpose of Construction: To construct a single family home
4. Length of Cut: Sidewalk + 3'
5. Width of Cut: 3'
6. Width of Existing Pavement: N/A
7. Type of Existing Roadway Surface: Asphalt Type of Curb: Asphalt
8. Type of Existing Sidewalk Surface: Asphalt Type of Shoulder: loam + seed
9. Date of Street Opening: From May 18 To May 20

I, the undersigned, hereby declare that I have read and agree to the Town of Acton Specifications for Regulating Construction with Public Ways dated February 4, 1969. I have deposited the required bond with the Town of Acton, and I covenant and agree that the Town may deduct from this amount the cost of repairs to the road surface, curbs, shoulders, walls or other features within the right-of-way including replacing bounds if not completed by me to the satisfaction of the Town Engineer within the specified time.

Witness my hand and seal,

Signature of Applicant: David C. Moulton

Special Instructions:

DIG-SAFE # 8719-39-84

See Dennis Ring for plan.

INSP. 5-13-87 DR.

2 BNDS MISSING

SHOULDER IS GRAVELED

SIDEWALK IS IN POOR CONDITION

INSP 4-20-88 DED

~~NO WORK DONE~~

CALL

INSP 6-16-88 DR

PIPE IN OK

Permit Issued: Date 5-13-87 By: Dennis P. Ring

Application Denied: Date By:

Work Inspected and Approved: Date 7-22-88 By: Dennis P. Ring

Fee 25.00

(over)

INDEXED

TOWN OF ACTON
TYPICAL DRIVEWAY 8
TRENCH DETAIL

FEB. 1969 NO SCALE

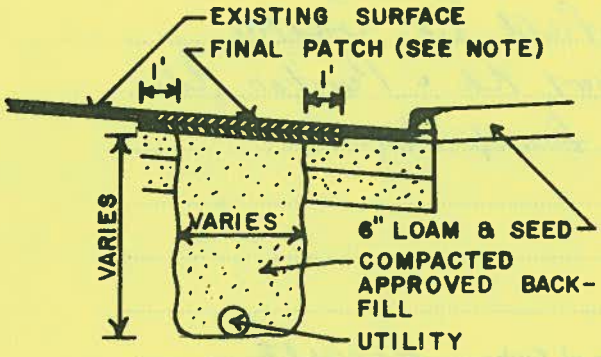

NOTE: 1. FINAL PATCH DEPTH
3" OIL TREATED ROADS
4" BIT. CONC. ROADS
2. SEE SPECIFICATIONS FOR FURTHER REQUIREMENTS

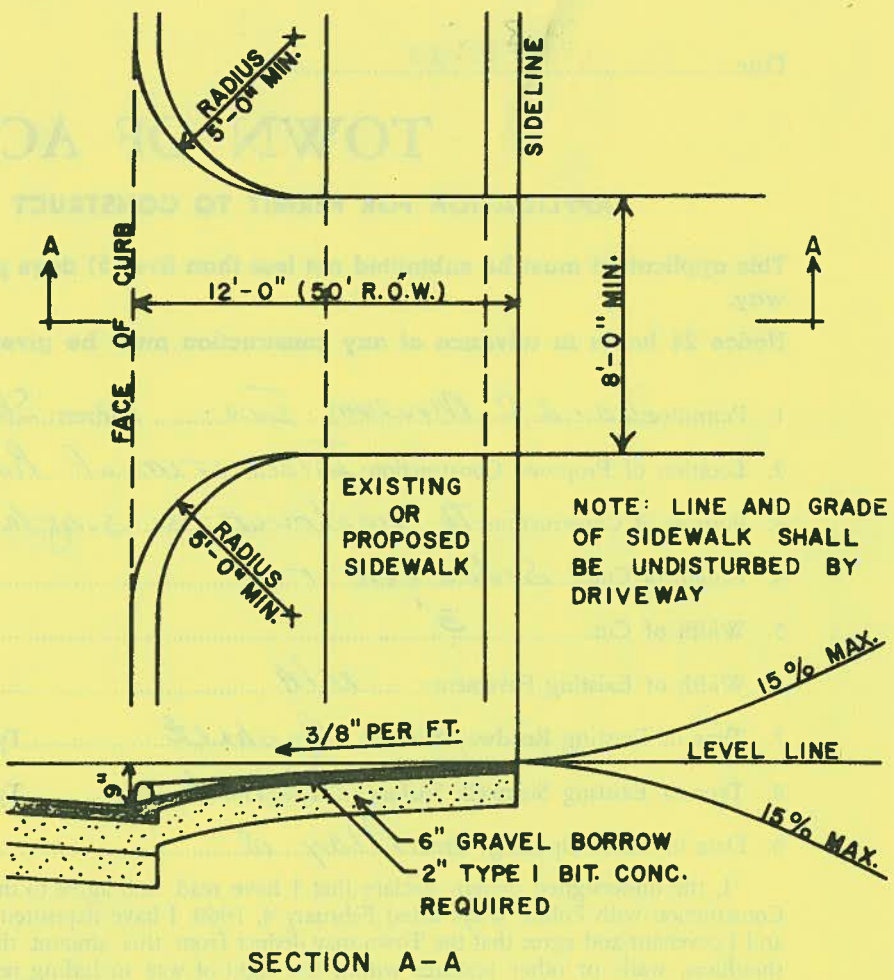

SECTION A-A

SKETCH

Date 5-13-87 Permit No. 87-30

TOWN OF ACTON

APPLICATION FOR PERMIT TO CONSTRUCT WITHIN A PUBLIC WAY

This application must be submitted not less than five (5) days prior to any Construction within a public way.

Notice 24 hours in advance of any construction must be given to the Town Engineer.

1. Permittee: David C. Moulton Inc Address: Skyfield Dr. Groton
2. Location of Proposed Construction: Intersection of Robert Rd & Puritan Rd.
3. Purpose of Construction: to construct a single family home
4. Length of Cut: Sidewalk + 3'
5. Width of Cut: 3'
6. Width of Existing Pavement: N/A
7. Type of Existing Roadway Surface: Asphalt Type of Curb: Asphalt
8. Type of Existing Sidewalk Surface: Asphalt Type of Shoulder: loam & seed
9. Date of Street Opening: From May 18 To May 20

I, the undersigned, hereby declare that I have read and agree to the Town of Acton Specifications for Regulating Construction with Public Ways dated February 4, 1969. I have deposited the required bond with the Town of Acton, and I covenant and agree that the Town may deduct from this amount the cost of repairs to the road surface, curbs, shoulders, walls or other features within the right-of-way including replacing bounds if not completed by me to the satisfaction of the Town Engineer within the specified time.
Witness my hand and seal,

Signature of Applicant David C. Moulton

Special Instructions:

DIG SAFE # 8719-39-84

Permit Issued: Date 5-13-87 By: Dennis P. Ryan

Application Denied: Date By:

Work Inspected and Approved: Date 7-22-88 By: Dennis P. Ryan

Fee ~~[illegible]~~ 25.00

(over)

TOWN OF ACTON
TYPICAL DRIVEWAY & TRENCH DETAIL

FEB. 1969 NO SCALE

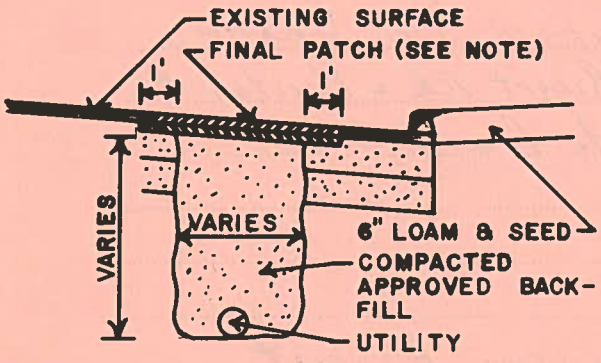

NOTE: 1. FINAL PATCH DEPTH
3" OIL TREATED ROADS
4" BIT. CONC. ROADS
2. SEE SPECIFICATIONS FOR FURTHER REQUIREMENTS

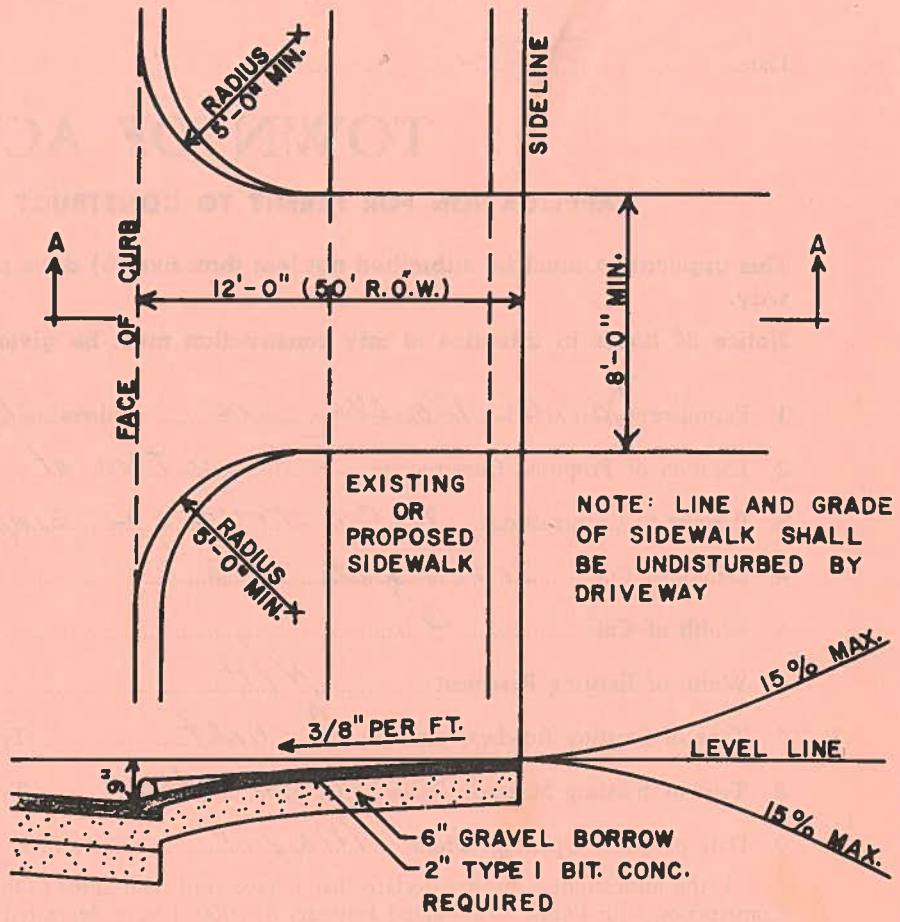

SECTION A-A

SKETCH

Date: 5/13/87

FROM: Engineering Department

TO: Town Treasurer

SUBJECT: Bond-Permit to Construct Within a Public Way

Please hold the enclosed Bond in the form of:

Certified Check # 21885 Bank UNION NATIONAL

Pass Book #_____ Bank_____

Other (Specify)_____

in the amount of $500.00 from (Applicant) DAVID C. MOULTON, INC.

as security for "Permit to Construct Within a Public Way" # 87-30

located at ROBERT RD. & PURITAN RD ; for authority

see Section IV-A, Specifications for Regulating Construction Within

Public Ways. This bond is to be held until released in writing by

this department.

Signed: David Albert

Town Engineer

DATE: 7/26/88

FROM: Engineering Department

TO: Town Treasurer

SUBJECT: Bond - Permit to Construct Within a Public Way

Please release the bond in the form of:

Certified Check # 21885 Bank UNB

Other (Specify) _____

in the amount of $500.00 to DAVID C. MOULTON

which is being held as security for "Permit to Construct Within a Public Way" # 87-30,

located at ROBERT RD & PURITAN;

for authority see Section II - A, Specifications for Regulating Construction Within Public Ways.

Work proposed under this permit has been satisfactorily completed.

ACCOUNT #: 796 AMOUNT: $ 500 00

SIGNED: David Moulton

MAILING ADDRESS: Skyfield Dr
Milton, MA

RELEASE

LOT 28 ROBERT RD

REC'D 3/24/87
REVIEW 4/10/87

- THIS PLAN OF SUBSURFACE DRAIN MUST BE SUBMITTED TO:
  (A) ENGINEER DEPT. FOR CONNECTION INTO PURITAN ROAD DRAINAGE
  (B) CONSERVATION COMMISSION FOR WORK WITHIN WETLAND
- PLEASE CLARIFY BENCH MARK.
- PLEASE ADD ENGINEER'S STAMP TO PLAN
- PLEASE ADD INFORMATION OF DRAIN DETAIL TO PLAN. (I.E. SIZE OF PIPE, STONE ETC.)
- WILL DRAIN EFFECTIVELY INTERCEPT GROUND WATER AT ROBERT ROAD SIDE OF PROPERTY?
- CLARIFY PLAN OF DRAIN ONLY

cc: CONSERVATION COMMISSION
✓ ENGINEERING DEPARTMENT.

L = 229.74'

2+50 inv. 200.45

L = 25.00'

2+00 inv. 200.70

6" PVC
Solid Wall
S = .0050

1+50 inv. 200.95

See Detail

1+00 inv. 201.20

0+50 inv. 201.45

0+00 inv. 201.70

ROBERT ROAD

100.00'

54.26'

144.99'

F.G. 206

F.G. 205

F.G. 207

GRD 1.5' Twin

GRD 7.5' Twin

Top Pipe 207.4

Top Pipe 207.8

Top Pipe 207.3

902

502

202

207

206

208

cation on plan indicated by ②

210 · 3" Fa over Field Sand

cast iron tee or baffle

4" cast iron pipe from building
minimum slope: ¼ inch per foot
